

STATE OF OREGON
WATER RESOURCES DEPARTMENT

REQUEST FOR WRITTEN APPROVAL TO USE CONSTRUCTION METHODS NOT
INCLUDED IN THE RULES AND REGULATIONS PRESCRIBING GENERAL STANDARDS
FOR THE CONSTRUCTION AND MAINTENANCE OF WELLS IN OREGON

Before approval can be considered the following questions must be answered.

Requests shall be submitted to the Watermaster Division, 3850 Portland Road,
NE, Salem, OR 97302.

Date: 2/10/97

Well Constructor Ivan Grossen

(1) Location of well: NW 1/4 S.E. 1/4 of Section 36,
Township S 5, Range 2W, Marion County.

Address at well site or nearest known address: 8626 Wabash Dr. N.E.
Brooks, OR

(2) Name and Address of Landowner: Valentine Miller
8626 Wabash Dr. N.E.
Brooks


(3) The distance to the nearest well and septic drainfield: 450' approx.

(4) The unusual conditions existing at the well site: well needs
To be sealed from 122-127' to prevent
Contamination of waters.

(5) The proposed construction methods that the well constructor or landowner
constructs. The well believes will be adequate for his particular well:
Perforate well from 122' to 127' and
pressure test 10" PVC pipe ^(class 2407) in place from
112' to 122' forcing cement through perforations
into formation outside of 12" casing.

w-up
remarks: bottom of well

(6) A diagram showing the pertinent features of the proposed well design and construction (attach additional sheet if necessary):

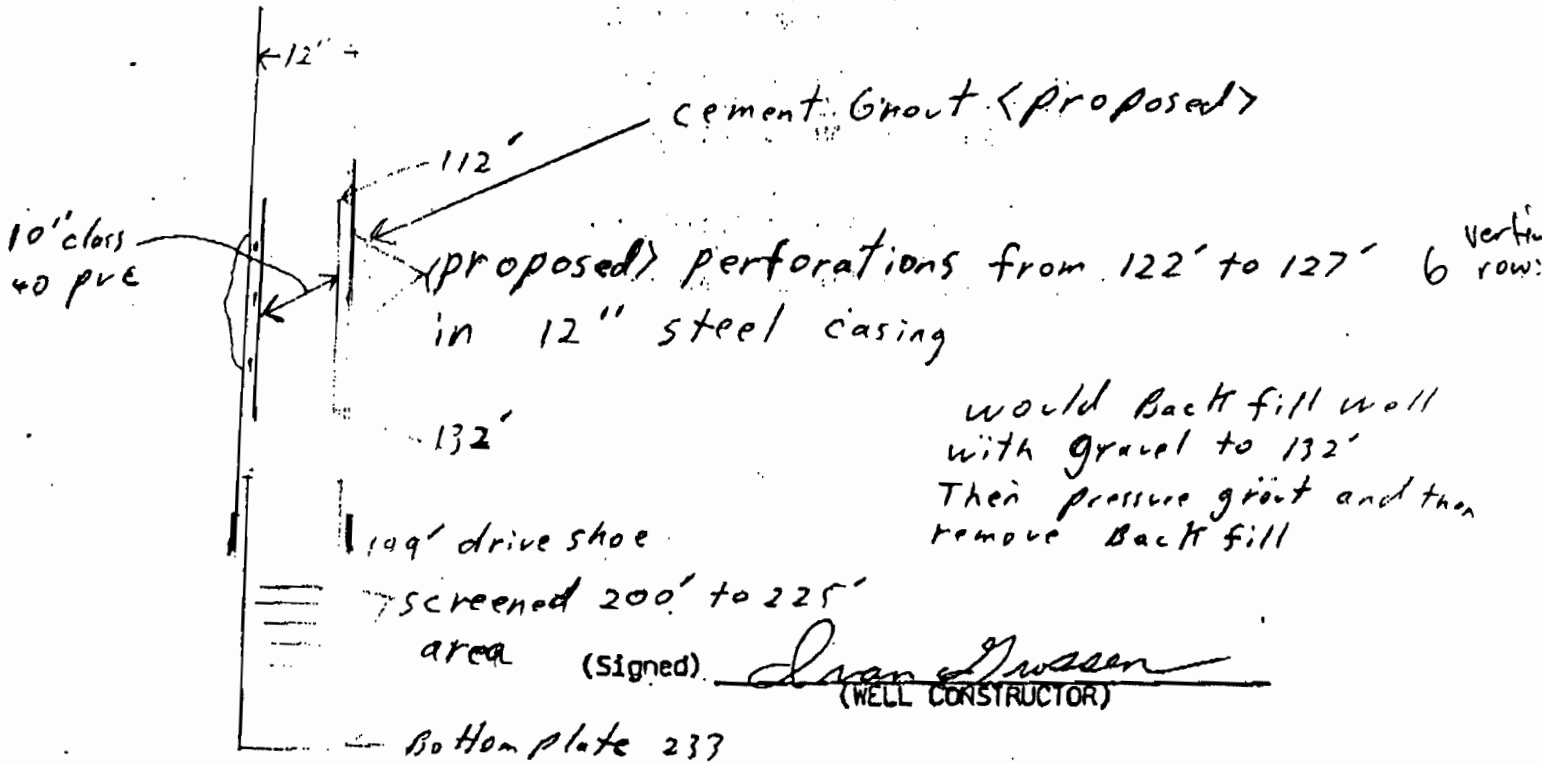

For Water Resources Department Use Only

Date: 4-23-97

Approved by: [Signature]

Denied by: _____

Remarks: _____

NOTE:

- (1) If approval, all other phases of construction must be in compliance with State Well Construction Standards.
- (2) If it should be determined at some future date that the well, due to its construction, is offering an avenue for pollution of the ground water body, it will be necessary for you to return to the site to correct any well deficiencies.
