

RECEIVED

MAR 05 1999

WATER RESOURCES DEPT.
SALEM, OREGON

STATE OF OREGON
WATER RESOURCES DEPARTMENT

REQUEST FOR WRITTEN APPROVAL TO USE CONSTRUCTION METHODS NOT INCLUDED IN THE RULES AND REGULATIONS PRESCRIBING GENERAL STANDARDS FOR THE CONSTRUCTION AND MAINTENANCE OF WELLS IN OREGON

Before approval can be considered the following questions must be answered.

Requests shall be submitted to the Watermaster Division, 3850 Portland Road, NE, Salem, OR 97310.

Date: 3-3-99

Well Constructor: Ed Brown

Waterwell Developing & Surveys

(1) Location of Well: NW 1/4 SW 1/4 of Section 22,

Township 4N, Range 24E, Morrow County.

Address at well site or nearest known address: 1/2 mile west of

Tower Rd Boardman

(2) Name and address of Landowner: Port of Morrow

SC# 43077

PO 200

Boardman, OR 97818

(3) The distance to the nearest well and septic drainfield: more than

1/2 mile

(4) The unusual conditions existing at the well site: Clay layer

at 605 ft needs a liner to

stand open

(5) The proposed construction methods that the well constructor or landowner constructing the well believes will be adequate for his particular well:

Request variance to install liner


above clay layer But not extend

up into 16" casing at 430 ft.

This would allow a 15" pump chamber

to 600 ft.

(6) A diagram showing the pertinent features of the proposed well design and construction (attach additional sheet if necessary):

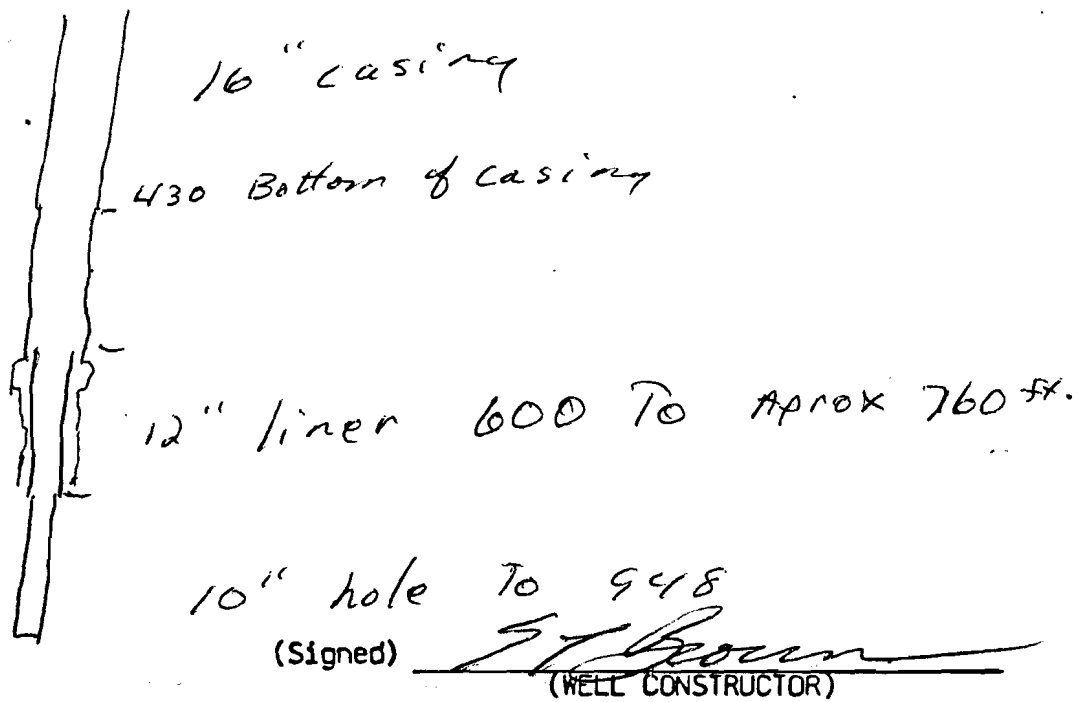

For Water Resources Department Use Only

Date: 3.26.99
Approved by: Michael J. McLeod
Denied by: _____
Remarks: Liner is installed so that it can be removed.

NOTE:

- (1) If approval, all other phases of construction must be in compliance with State Well Construction Standards.
- (2) If it should be determined at some future date that the well, due to its construction, is offering an avenue for pollution of the ground water body, it will be necessary for you to return to the site to correct any well deficiencies.
