



Oregon

John A. Kitzhaber, M.D., Governor

Water Resources Department

Commerce Building
158 12th Street NE
Salem, OR 97301-4172
(503) 378-3739
FAX (503) 378-8130

February 6, 2001

Patrick Wallace
Wallace Drilling
1707 S. W. 18th
Pendleton, OR 97801

Dear Pat:

Attached is a copy of the following approved special standard:

1. Gene Byers (start card number ~~97058~~) 129885

Special standard requests must be submitted to the Department within (3) days from the date an oral approval is granted. Failure to do so in the future may result in the special standard being denied at a later date even if an oral approval was given. If a special standard request is denied, the Department will most likely require that any well that is not constructed to standard be abandoned. If you have any questions concerning this letter, please contact me at the address or phone number listed above, or by e-mail at michael.l.mccord@wrdd.state.or.us.

Sincerely,

Michael L. McCord
Well Construction Specialist

c: Brian Mayer, NC Region Well Inspector
Drillers File



JD # 38619

FINAL ORDER
Oregon Water Resources Department

REQUEST FOR WRITTEN APPROVAL TO USE CONSTRUCTION METHODS NOT INCLUDED IN OREGON ADMINISTRATIVE RULES 690-200 THROUGH 690-240

Before request can be considered, the following must be answered. Requests shall be submitted to the Well Construction Specialist, Water Resources Department. Requests may also be considered by the appropriate Regional Manager.

Date of request: 9-5-2000 Oral approval date (if applicable): 9-5-2000

Bonded Well Constructor (name, license #, and mailing address): Patrick Wallace

#1218 1707 SW 18th Pendleton Or

(1) Location of Well: SW 1/4 SW 1/4 of Section 32,
Township 2N N1S, Range 14E E1W, Wasco County.

Address at well site: 3693 Fifteen Mile Rd
The Deller Or

(2) Start Card Number(s): 97058

(3) Name and Address of Land Owner: Gene Byers

same


(4) Distance to the nearest well, septic tank or drainfield (if water supply well): 1000+

(5) The unusual conditions which necessitate this request: caving formation
bottom 24'

(6) The proposed construction methods that the well constructor believes will be adequate for this well (attach additional pages if needed)
install 40' liner from 535' to
495'

RECEIVED
JAN 31 2001
WATER RESOURCES DEPT
SALEM, OREGON

- (7) Diagram showing the pertinent features of the proposed well design and construction (attach additional pages if needed):

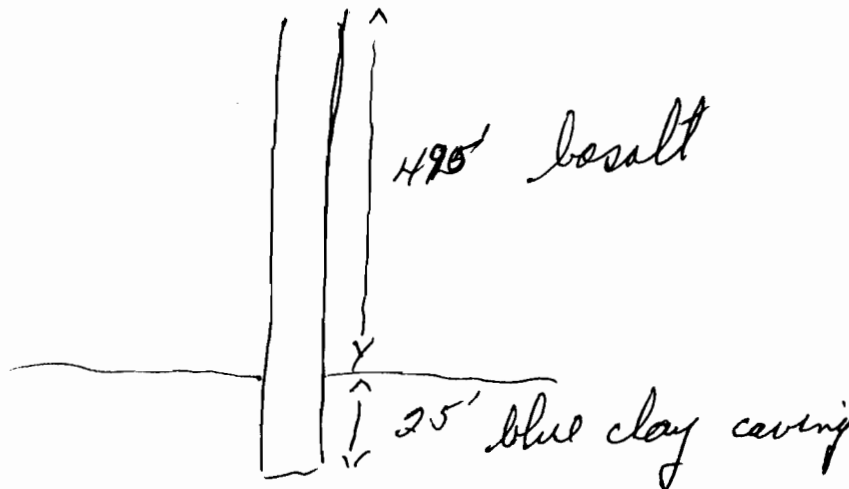

PLEASE NOTE:

- (1) If approved, all other phases of well construction must comply with the appropriate standards described in OAR 690-200 through 690-240.
- (2) If it should be determined at some future date that the well, due to its construction, is allowing groundwater contamination, waste or loss of artesian pressure, the undersigned shall return to the site and rectify the problem.
- (3) If oral approval was granted, a written request must be submitted to the Department either within three (3) working days of the date of oral approval or prior to the completion of the associated well work. Failure to submit a written request as described above may void prior approval.

I have read and understand the above information. I further attest that the information provided is accurate to the best of my knowledge.

Bonded Constructor Signature: Patrick Wallace

For Water Resources Department Use Only

Date: 2-1-01
Approved by: Michael J. [Signature] Denied by: _____
Remarks: _____
