

Wash 52210

WASH 52210

RECEIVED

STATE OF OREGON WATER SUPPLY WELL REPORT

WELL I.D.# L02188

MAY 30 1997

95178

WATER RESOURCES DEPT. SALEM, OREGON

Instructions for completing this report are on the last page of this form.

(1) OWNER: Well Number Elligsen Name City of Wilsonville Address 30000 SW Town Center Loop East City Wilsonville State OR Zip 97070

(2) TYPE OF WORK [X] Alteration (repair/recondition)

(3) DRILL METHOD: [X] Other Pump Rig

(4) PROPOSED USE: [X] Community

(5) BORE HOLE CONSTRUCTION: Special Construction approval [X] Yes Depth of Completed Well 779 ft.

Table with columns: Diameter, From, To, Material, From, To, Sacks or pounds. Content: NOT CHANGED

How was seal placed: Method [] A [] B [] C [] D [] E

(6) CASING/LINER: Casing: 12 +20 ? ? [X] Steel [X] Plastic [X] Welded [] Threaded Liner: New 10 0 576 .250 [X] exist: 10 576 ? ? [X]

(7) PERFORATIONS/SCREENS: [X] Perforations Method Rotary Star Wheel

(8) WELL TESTS: Minimum testing time is 1 hour [X] Pump Yield gal/min See Attached Graphs

Temperature of water ~ 55°F Depth Artesian Flow Found Was a water analysis done? [] Yes By whom

(9) LOCATION OF WELL by legal description: County Washington Latitude Longitude Township 3S N or S Range 1W E or W. WM. Section 1 SE 1/4 SW 1/4 Tax Lot 700 Lot Block Subdivision Street Address of Well (or nearest address) 7600 SW Elligson Wilsonville, OR 97070

(10) STATIC WATER LEVEL: 192 ft. below land surface. Date 5/14/97

(11) WATER BEARING ZONES: Depth at which water was first found NA - No Drilling

Table with columns: From, To, Estimated Flow Rate, SWL. Content: NA - No Drilling

(12) WELL LOG: Ground Elevation Approx. 350'

Table with columns: Material, From, To, SWL. Content: No Drilling - Alteration Included: 1) Perforating existing 10" liner 2) Developing & bailing 3) Adding a new upper 10" liner 4) Test Pumping

Date started 4/10/97 Completed 5/19/97


(unbonded) Water Well Constructor Certification: I certify that the work performed on the construction, alteration, or abandonment of this well is in compliance with Oregon water supply well construction standards.

(bonded) Water Well Constructor Certification: I accept responsibility for the construction, alteration, or abandonment work performed on this well during the construction dates reported above.

MAY 30 1997

WATER RESOURCES DEPT.
SALEM, OREGON

WILSONVILLE ELLIGSON WELL TEST
by Schneider Drilling Co. 5/14-15/97 - SWL 192' BGS
304 GPM first 1470 minutes then @ 362 GPM

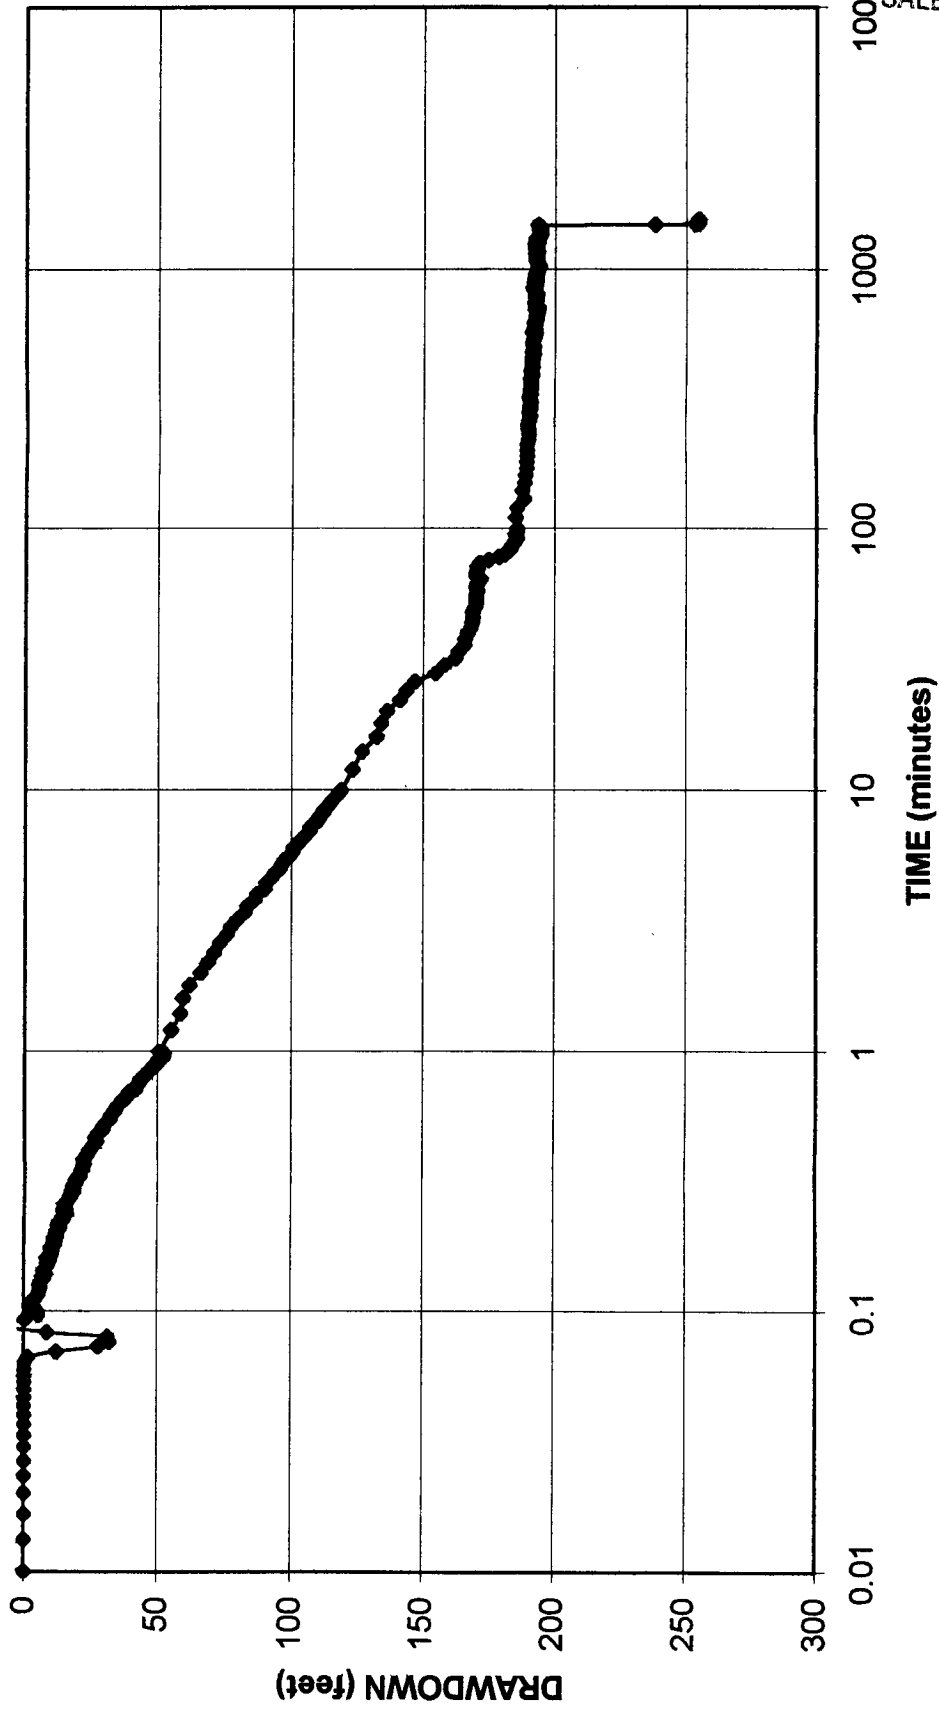

MAY 30 1997

WATER RESOURCES DEPT
SALEM, OREGON

WILSONVILLE ELLIGSON WELL RECOVERY
by Schneider Drilling Co. 5/15-19/97
Pumped @ 304 GPM for 1470 min.; then 362 GPM for 85 min.

