

RECEIVED

MAY 30 1989

STATE OF OREGON
WATER RESOURCES DEPARTMENT

WATER RESOURCES DEPT.
SALEM, OREGON

REQUEST FOR WRITTEN APPROVAL TO USE CONSTRUCTION METHODS NOT
INCLUDED IN THE RULES AND REGULATIONS PRESCRIBING GENERAL STANDARDS
FOR THE CONSTRUCTION AND MAINTENANCE OF WELLS IN OREGON

Before approval can be considered the following questions must be answered.

Requests shall be submitted to the Watermaster Division, 3850 Portland Road,
NE, Salem, OR 97310.

Date: 5-15-89 - is the date I called in and talked with Mr. King on this.

Well Constructor: [Redacted]
11364 Evergreen Rd. N.E., Silveston, Ore. 97381

(1) Location of Well: N.E. 1/4 S.W. 1/4 of Section 18,
Township 5 S, Range 1 E, Clackamas County.

Address at well site or nearest known address: 6358 S. Schneiders Rd.
Woodburn, Ore. 97071

(2) Name and address of Landowner: Robert E. Johnson
27571 S. Rings Rd.
Mulino, Ore. 97042

(3) The distance to the nearest well and septic drainfield: over 100 ft.


(4) The unusual conditions existing at the well site: We encountered &
caving formation around 15 ft. & installed a 10" casing until
we were thru drilling & then pumped the water out the rear in -

(5) The proposed construction methods that the well constructor or landowner
constructing the well believes will be adequate for his particular well:

the annular space & being as the walls were wet we
didn't want to pour the dry granular down & needed
to put in the bentonite slurry. That is what I called
you about, but I'm sorry that I forgot about it &
I didn't call in until after we had put in the slurry.
you said to make a note & send it along with the
log & that is what this is for. Thank you - over.

sc10686
#296
W
SM
CLAC 2538

(6) A diagram showing the pertinent features of the proposed well design and construction (attach additional sheet if necessary):

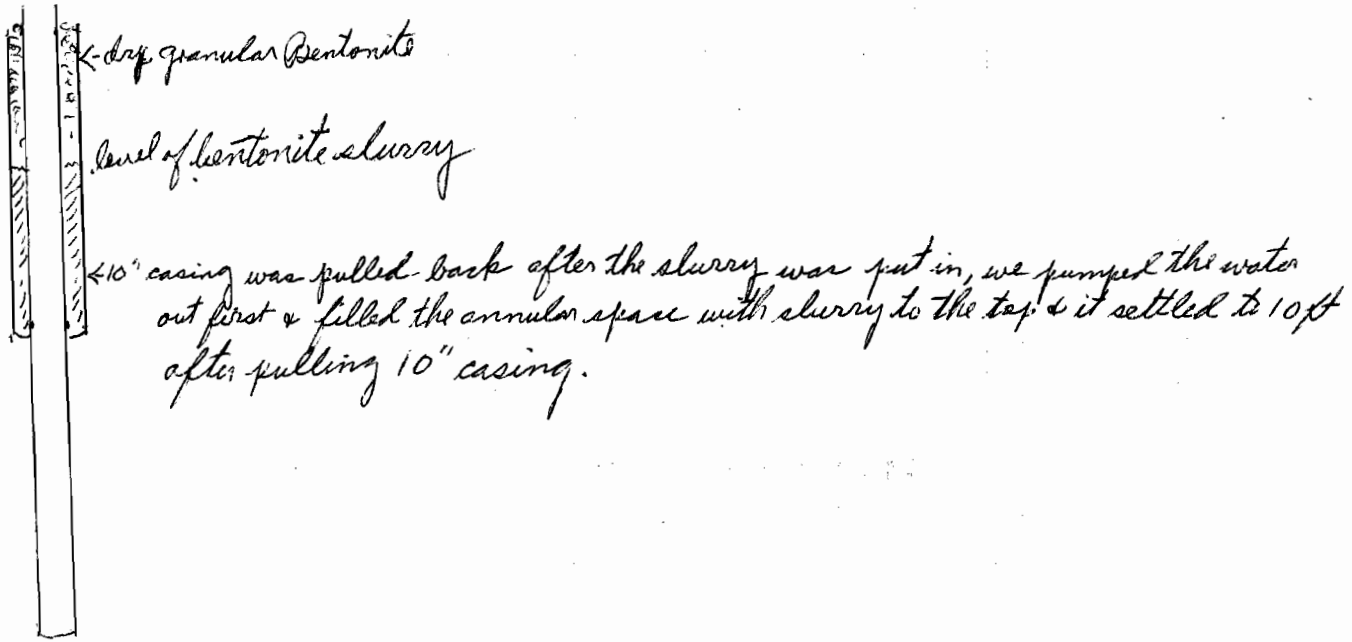

(Signed) Paul R. Stadel
(WELL CONSTRUCTOR)

For Water Resources Department Use Only

Date: 5-30-89

Approved by: [Signature]

Denied by: _____

Remarks: _____

NOTE:

- (1) If approval, all other phases of construction must be in compliance with State Well Construction Standards.
- (2) If it should be determined at some future date that the well, due to its construction, is offering an avenue for pollution of the ground water body, it will be necessary for you to return to the site to correct any well deficiencies.

8415D
