



Oregon

John A. Kitzhaber, M.D., Governor

Water Resources Department

Commerce Building
158 12th Street NE
Salem, OR 97310-0210
(503) 378-3739
FAX (503) 378-8130

April 20, 1999

en

Steven N. Stadel
Westerburg Drilling
36728 S. Kropf Road
Molalla, OR 97038

Dear Steve:

Attached is the approved copy of the following special standard:

1. Robert Fessler - (start card number 119212)

If you have any questions concerning this letter, please contact me at the address or phone number listed above.

Sincerely,

Michael L. McCord
Well Construction Specialist

c: Richard Edwards, Well Inspector



Oregon Water Resources Department

REQUEST FOR WRITTEN APPROVAL TO USE CONSTRUCTION METHODS NOT INCLUDED IN OREGON ADMINISTRATIVE RULES 690-200 THROUGH 690-240

Before request can be considered, the following must be answered. Requests shall be submitted to the Well Construction Specialist, Water Resources Department. Requests may also be considered by the appropriate Regional Manager.

Date of request: 4-20-99

Bonded Well Constructor (name, license and mailing address): STEVEN N.

STADEL 36728 S. KROFF RD. MOLALA, OR. 97038 Lic. # 688

(1) Location of Well: NE 1/4 NE 1/4 of Section 28, Township 55,

Range 1W, MARION County.

Address at well site: 13118 MCKEE SCHOOL RD

WOODBURN OR.

(2) Start Card Number(s): 119212

(3) Name and Address of Land Owner: ROBERT FESSLER / WOODBURN

NURSERY & AZALEAS INC.

(4) The distance to the nearest well, septic tank or drainfield (if water supply well): MORE

THAN 100'

(5) The unusual conditions which necessitate this request: BRINGING THIS

WELL INTO COMPLIANCE WITH PERMIT CONDITIONS FOR

PERMIT # G-14762 WELL # MARI 2031

(6) The proposed construction methods that the well constructor believes will be adequate for this well (attach additional pages if needed)

ABANDON LOWER PORTION OF EXISTING WELL BY

PUMPING CEMENT GROUT INTO BOREHOLE & OUT THRU.

EXISTING 8" SCREEN. CEMENT GROUT WILL BE PUMPED CONTINUOUSLY
UP TO 145 B.G.S. BECAUSE PERFORATING THE EXISTING 8" CASING
WILL CAUSE SCREEN ASSEMBLY TO PUSH OUT OF WELL,

W-27
 remark - abandon bottom

(7) Diagram showing the pertinent features of the proposed well design and construction (attach additional pages if needed):

It is Proposed To Add No More Perforations.

SEE ATTACHED DRAWING.

**Westerberg Drilling, Inc.
36728 S. Kropf Rd.
Molalla, OR 97038
829-2526**

PLEASE NOTE:

- (1) If approved, all other phases of well construction must comply with the appropriate standards described in OAR 690-200 through 690-240.
- (2) If it should be determined at some future date that the well, due to its construction, is allowing groundwater contamination, waste or loss of artesian pressure, the undersigned shall return to the site and rectify the problem.
- (3) If verbal approval was granted, a written request must be submitted to the Department either within three (3) working days of the date of verbal approval or prior to the completion of the associated well work. Failure to submit a written request as described above may void prior approval.

I have read and understand the above information. I further attest that the information provided is accurate to the best of my knowledge.

Bonded Constructor Signature: *Stev N. Stadel*

For Water Resources Department Use Only


Date: *4.20.99*

Approved by: *Michael M. East* Denied by: _____

Remarks: _____ revised: 4-96

MARI - # 2031

Permit App. # G-14762

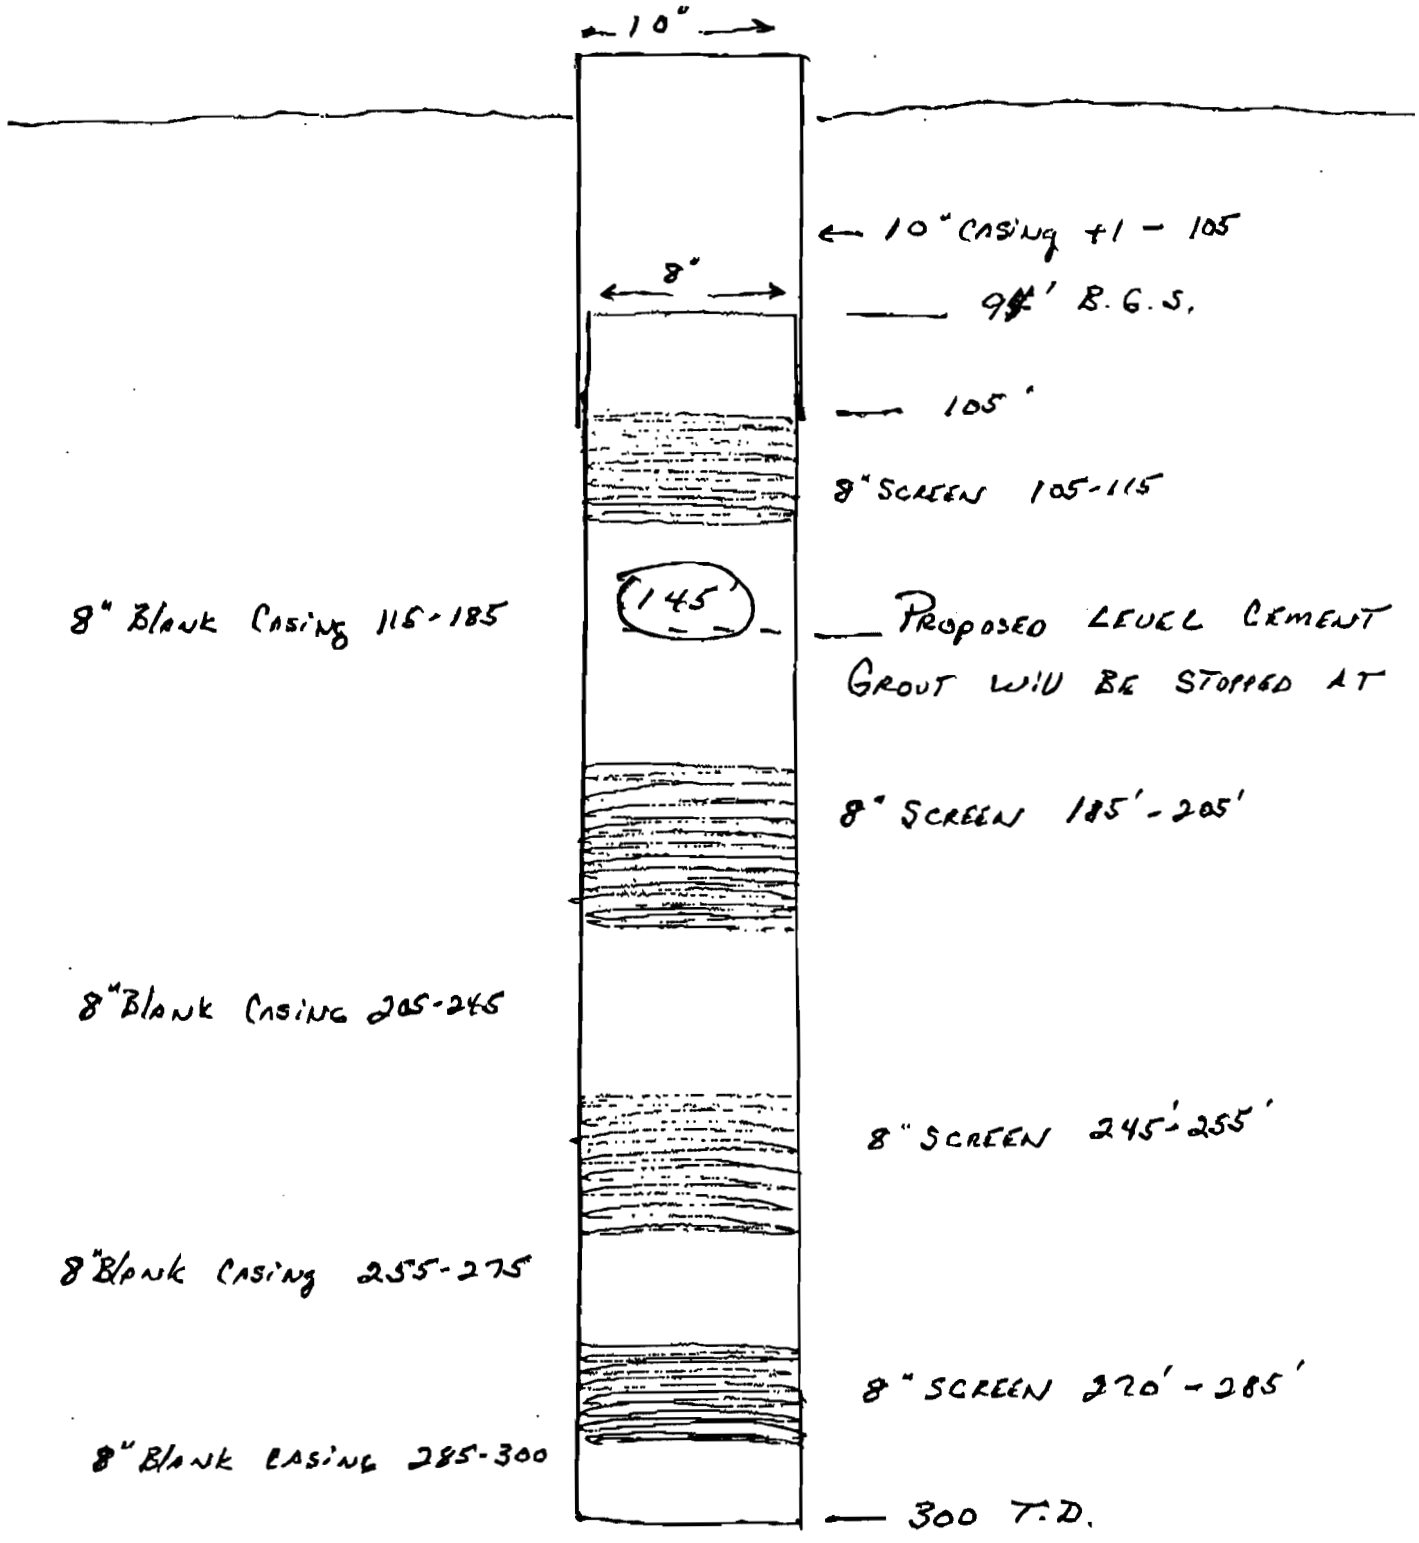

Westerberg Drilling, Inc.
 36728 S. Kropf Rd.
 Molalla, OR 97038
 829-2526
