

e v 9/20/02

STATE OF OREGON
WATER RESOURCES DEPARTMENT

JAN 04 1993

REQUEST FOR VARIANCE OR EXCEPTION TO THE RULES AND REGULATIONS
FOR CONSTRUCTION OF A WATER WELL*.

WATER RESOURCES DEPT.
SALEM, OREGON

Before approval can be considered, all of the following questions must be answered.

Requests shall be submitted to the Watermaster in the county in which the well is to be constructed.

THE ORIGINAL OF THIS FORM MUST BE SIGNED BY THE WATERMASTER AND FORWARDED TO THE SALEM OFFICE.

Date: 9-25-92

Water Well Constructor: Van Meter and Despain Well Drlg.
Larry Despain

(1) Purpose of Well Construction: Irrigation

(2) Location of Well: SE 1/4 SW 1/4 of Section 21, Township 34S
Range 8E, Klamath County.

Address at well site or nearest known address: 555M Sprague River Hwy.
Chiloquin, Or. 97624

(3) Name and address of Landowner: Donald Chaix
HC 63 Bx 555M
Chiloquin, Or. 97624

(4) The distance to the nearest well and septic drainfield: _____

(5) The unusual conditions existing at the well site: Well needs to
be re-sealed to 50' due to the pressure of the
high SWL @ 6'4". This will keep the water from moving
up the outside of the casing and escaping into the 24' to 34'

(6) The reasons that compliance to the rules and regulations for minimum ^{permeable} standards will not result in a satisfactory well: layer.

35198 BY [Signature]


W-OT

(* In accordance with Oregon Administrative Rules Chapter 690, Division 60, Article 60.040)

(7) The proposed standards that the water well constructor or landowner constructing the well believes will be adequate for his particular well:

- (1.) Place a drillable plug at 70'. (2.) Backfill with Cement to 50'. (3.) Let it set. (4.) Perforate the casing from 20' to 50'. (5.) Pressure grout the area from 20' to 50' with Cement grout. (6.) Let set completely. (7.) Drill it all out to Complete.

(8) A diagram showing the pertinent features of the proposed well design and construction (attach additional sheet if necessary):

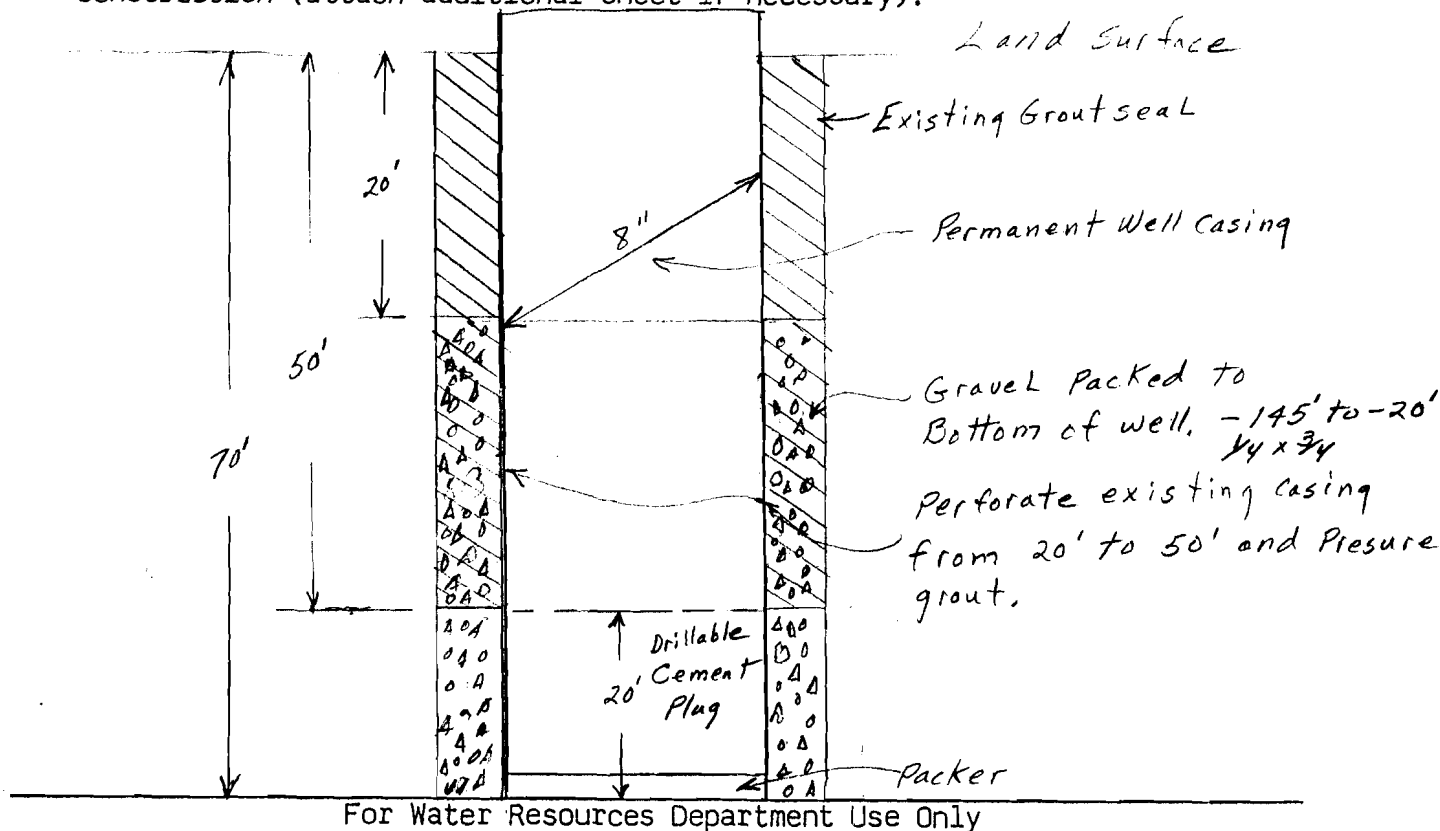

Date: 9-29-92

Approved by: _____

Denied by: J.A.C.

Remarks: Salem says Larry must hold 50 PSI for 24 hrs, with the well being gravel packed.

NOTE:

- (1) If approved, all other phases of construction must be in compliance with State Well Construction Standards.
- (2) If it should be determined at some future date that the well, due to its construction, is offering an avenue for pollution of the ground water body, it will be necessary for you to return to the site to...
