



Oregon

John A. Kitzhaber, M.D., Governor

Water Resources Department

Commerce Building
158 12th Street NE
Salem, OR 97310-0210
(503) 378-3739
FAX (503) 378-8130

December 1, 1998

Steve Bland
Skyles Well Drilling, Inc.
1169 Molalla Ave.
Oregon City, OR 97045

Dear Steve:

Please find enclosed copies of the following approved special standards:

1. Zig Zag Water Co-op (start card number 115778)
2. S. D. Deacon (start card number 119436)

If you have any questions concerning this letter, please contact me at the address or phone number listed above, or by e-mail at michael.l.mccord@wrdd.state.or.us.

Sincerely,

Michael L. McCord
Well Construction Specialist

c: Richard Edwards, Well Inspector

Oregon Water Resources Department

REQUEST FOR WRITTEN APPROVAL TO USE CONSTRUCTION METHODS NOT
INCLUDED IN OREGON ADMINISTRATIVE RULES 690-200 THROUGH 690-210

RECEIVED

NOV 02 1998

WATER RESOURCES DEPT.
SALEM, OREGON

Before request can be considered, the following must be answered. Requests shall be submitted to the Well Construction Specialist, Water Resources Department. Requests may also be considered by the appropriate Regional Manager.

Date of request: October 6, 1998 **SKYLES DRILLING, INC.**

Bonded Well Constructor (name, license and mailing address): Steven C. Bland

#1592 1169 Molalla Ave., Oregon City, OR 97045

(1) Location of Well: NW 1/4 SW 1/4 of Section 34, Township 2 South,
Range 7 East, Clackamas County.

Address at well site: 23777 E. Rockwood Creek Ln.
Zig Zag, OR 97049

(2) Start Card Number(s): 115778

(3) Name and Address of Land Owner: Zig Zag Water Co-op
PO Box 268, Rhododendron, OR 97049

(4) The distance to the nearest well, septic tank or drainfield (if water supply well):
Over 100 Feet


(5) The unusual conditions which necessitate this request: 10 INCH CASING
WON'T JACK OUT ALL THE WAY.

(6) The proposed construction methods that the well constructor believes will be adequate for this well (attach additional pages if needed)

DIG Minimum 10 feet (Deeper if possible)
Cut off 10 inch casing and remove after
pumping in upper seal. Leaving balance of 10
inch with the drive shoe in the hole.

w-up

- (7) Diagram showing the pertinent features of the proposed well design and construction (attach additional pages if needed):

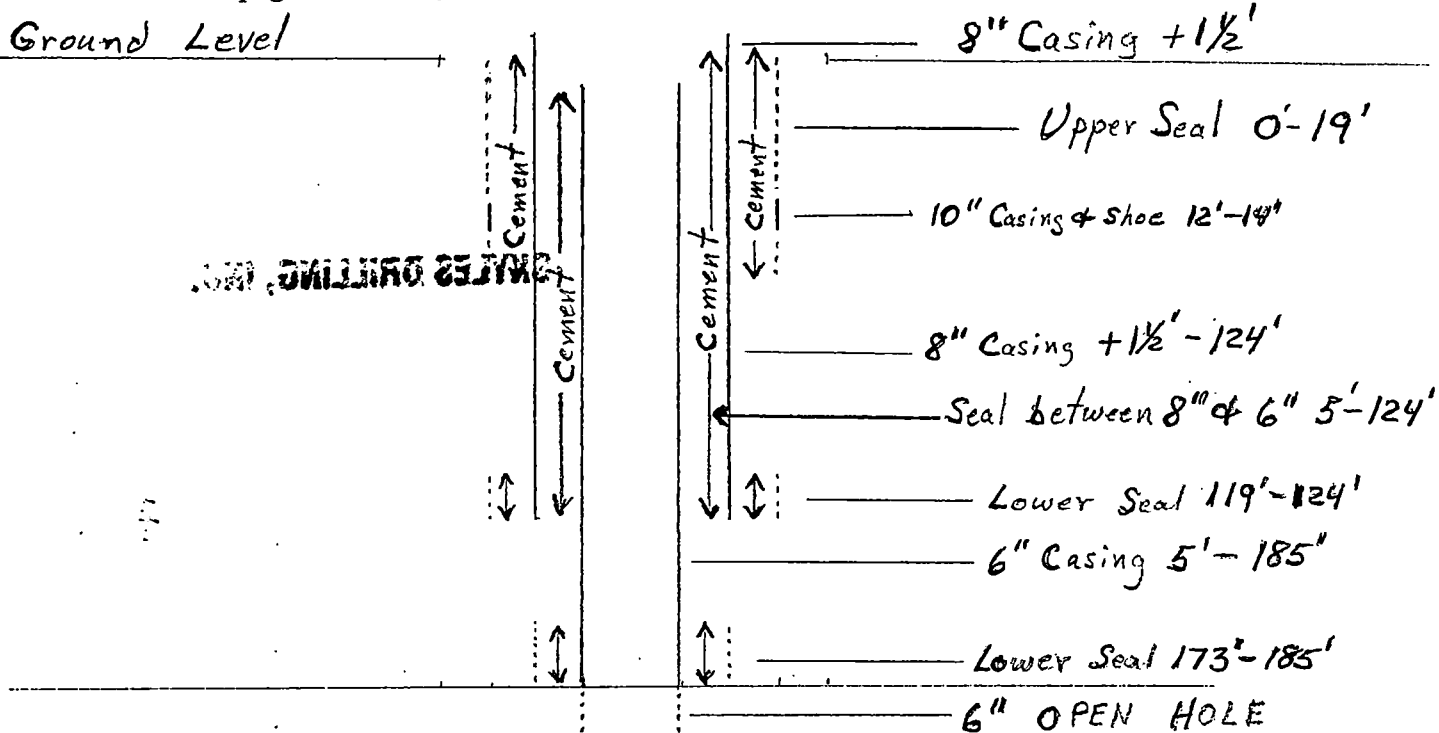

PLEASE NOTE:

50gpm Flowing Artesian
Artesian Pressure 20 lbs.

- (1) If approved, all other phases of well construction must comply with the appropriate standards described in OAR 690-200 through 690-240.
- (2) If it should be determined at some future date that the well, due to its construction, is allowing groundwater contamination, waste or loss of artesian pressure, the undersigned shall return to the site and rectify the problem.
- (3) If verbal approval was granted, a written request must be submitted to the Department either within three (3) working days of the date of verbal approval or prior to the completion of the associated well work. Failure to submit a written request as described above may void prior approval.

I have read and understand the above information. I further attest that the information provided is accurate to the best of my knowledge.

Bonded Constructor Signature: Steven C. Blund **SKYLES DRILLING, INC.**

For Water Resources Department Use Only

Date: 11.30.98

Approved by: Michael J. McLeod Denied by: _____

Remarks: _____ revised: 4-96
