

RECEIVED

JUL 08 2003

WATER RESOURCES DEPT.
SALEM, OREGON

Oregon Water Resources Department

REQUEST FOR WRITTEN APPROVAL TO USE CONSTRUCTION METHODS NOT INCLUDED IN OREGON ADMINISTRATIVE RULES 690-200 THROUGH 690-240

Before the request can be considered, this form must be completed. Requests shall be submitted to the Well Construction Specialist, Water Resources Department, 158.12th Street NE, Salem OR 97301. Requests may also be considered by the appropriate Regional Manager.

Date of request: 7-3-03 Oral approval date (if applicable): _____

Bonded Well Constructor (name, license #, and mailing address): Chris Humphries

#1796 - 1775 Henderson Ave, Eugene, OR. 97403.

(1) Location of Well: NW 1/4 NW 1/4 of Section 18,

Township 5 N(S), Range 1 E(W), MORRIS County

Address at well site: 515, Stetter Ave & 828 Parr Rd

(2) Start Card Number(s)(for work to be done): 79459 & 79453.

(3) Name and Address of Land Owner: City of Woodburn - 190 Garfield st
Woodburn, OR, 97071

(4) Distance to the nearest septic tank, drainfield, closed sewage line (if water supply well)
not sure - this plan was implemented by city

(5) The unusual site conditions which necessitate this request: The use of
alternative technologies or methods (reverse circulator drilling
method)

(6) The proposed construction methods that the bonded well constructor believes will be adequate for this well: (attach additional pages if needed)

We want to install a 188 wall conductor casing
24" nominal pipe size to a depth of 20' this will be installed
and grouted in a 30" bore hole. The conductor casing will
facilitate drill with a reverse circulator drill method - upon final
sealing of the well grout will be formed between the final
well casing (16" .375 wall) and the 24" conductor. The seal
will be continuous from approx 200' to surface including
annulus between 16 and 24.

- (7) Diagram showing the pertinent features of the proposed well design and construction:
(attach additional pages if needed)


please see attached drawing (stamped)

PLEASE NOTE:

- (1) If approved, all other phases of well construction must comply with the appropriate standards described in OAR 690-200 through 690-240.
- (2) If it should be determined at some future date that the well, due to its construction, is allowing ground water contamination, waste or loss of artesian pressure, the undersigned shall return to the site and rectify the problem.
- (3) If oral approval was granted, a written request must be submitted to the Department either within three (3) working days of the date of oral approval or prior to the completion of the associated well work. Failure to submit a written request as described above may void prior oral approval.

I have read and understand the above information. I further attest that the information provided is accurate to the best of my knowledge.

Bonded Constructor Signature: _____





RECEIVED

JUL 08 2003

WATER RESOURCES DEPT.
SALEM, OREGON

revised 06/2003

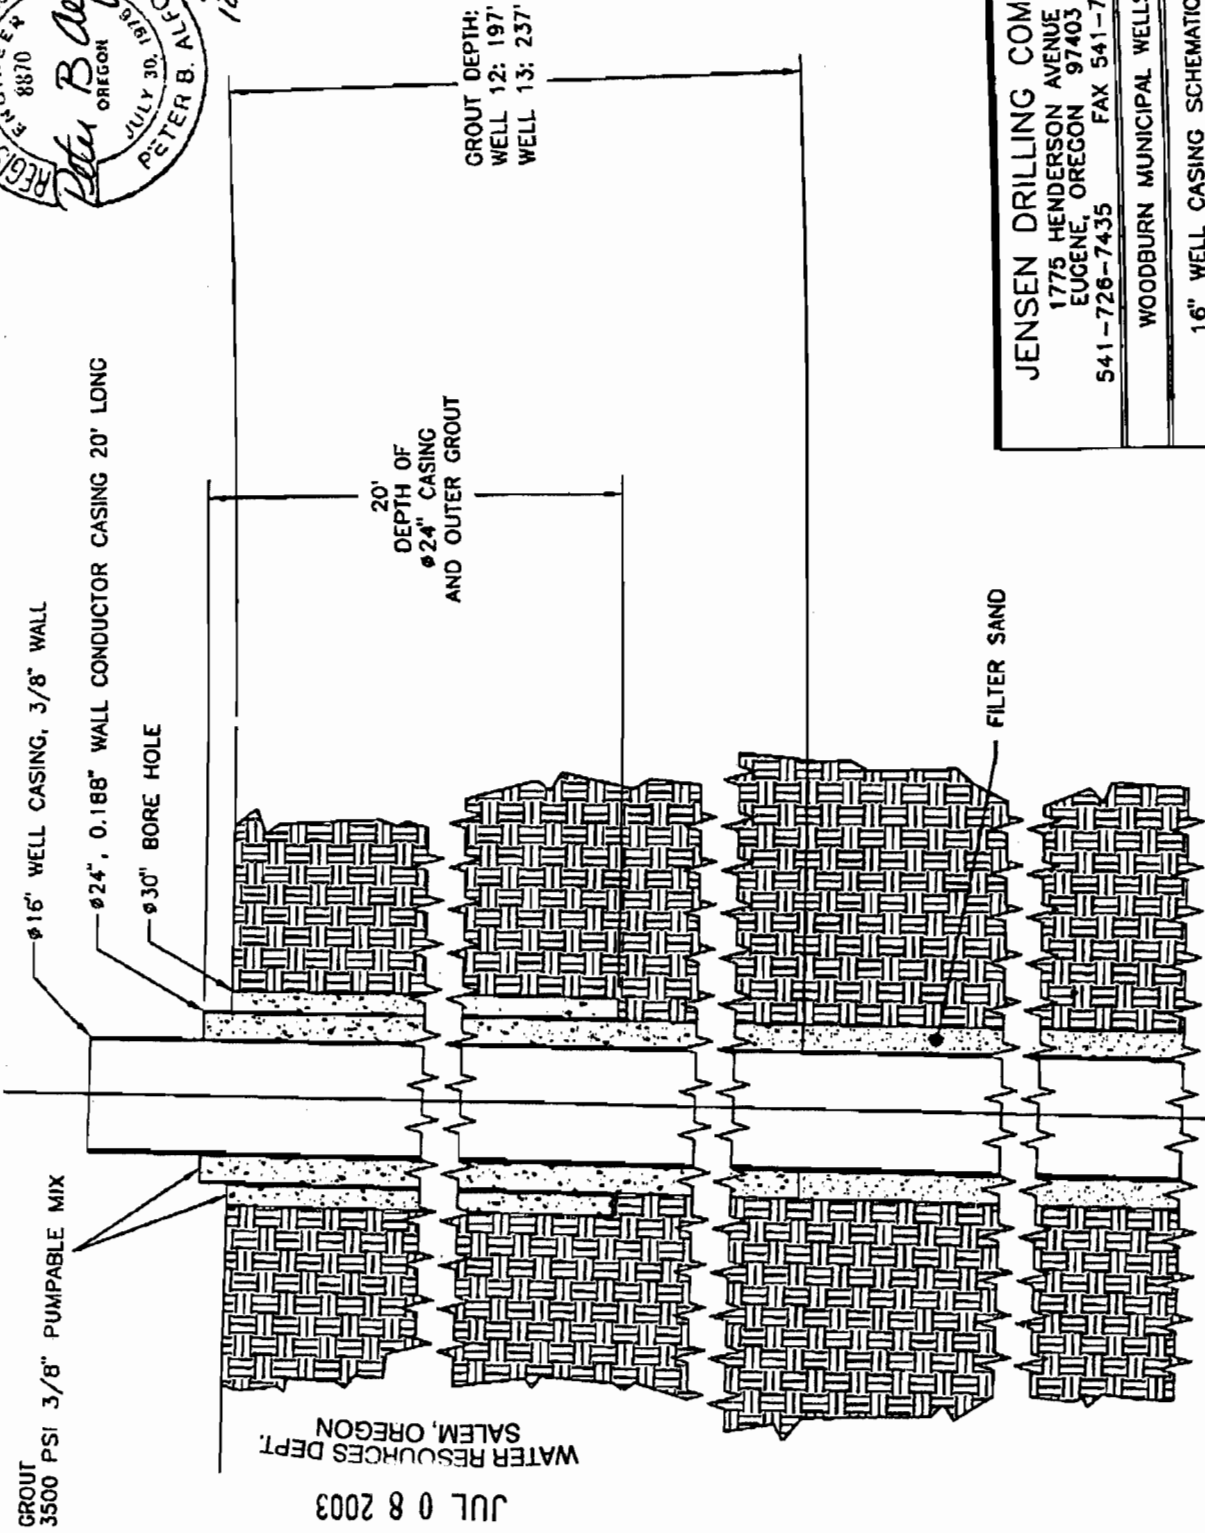

JENSEN DRILLING COMPANY
1775 HENDERSON AVENUE
EUGENE, OREGON 97403
541-726-7435 FAX 541-726-6140

WOODBURN MUNICIPAL WELLS

16" WELL CASING SCHEMATIC
WELLS 12 AND 13

JUNE 20, 2003 PBA
SHEET 1 OF 1

DRAWING 16WELLS

WATER RESOURCES DEPT.
SALEM, OREGON

RECEIVED
JUL 08 2003
