FINAL ORDER
Oregon Water Resources Department

REQUEST FOR WRITTEN APPROVAL TO USE CONSTRUCTION METHODS NOT INCLUDED IN OREGON ADMINISTRATIVE RULES 690-200 THROUGH 690-240

Before request can be considered, the following must be answered. Requests shall be submitted to the Well Construction Specialist, Water Resources Department. Requests may also be considered by the appropriate Regional Manager.

Date of request: 3/26/01 **Oral approval date (if applicable):** 3/26/01

Bonded Well Constructor (name, license #, and mailing address): Jeff Hendrickson #1553

77425 S.6th Street Cottage Grove, Oregon 97424

(1) Location of Well: _____ 1/4 _____ 1/4 of Section 28,

Township 21 N/(S) Range 3 E/(W) Lane County.

Address at well site: Cottage Grove Dam Between Dam and Highway

Cottage Grove, Oregon 97424

(2) Start Card Number(s): W136065

(3) Name and Address of Land Owner: US Army Corps of Engineers

75819 Shortridge Hill Rd. Cottage Grove, Oregon 97424

(4) Distance to the nearest well, septic tank or drainfield (if water supply well): 500'

(5) The unusual conditions which necessitate this request: Water Smelled like sulfer at 95' and needed to seal off top water.

(6) The proposed construction methods that the well constructor believes will be adequate for this well (attach additional pages if needed)

Installed 4" liner at set shell trap at 110' and cement up anular from 110' up to top.

W-OT
remark: shale trap - repair

Oregon
John A. Kitzhaber, M.D., Governor

Water Resources Department
Commerce Building
158 12th Street NE
Salem, OR 97301-4172
(503) 378-3739
FAX (503) 378-8130

April 3, 2001

Jeff Hedrickson
Hedrickson Well Drilling
77425 S. 6th Street.
Cottage Grove, OR 97424

Dear Jeff:

Attached is a copy of the following approved special standard:

1. US Army Corps of Engineers (start card numbers 136065)


If you have any questions concerning this letter, please contact me at the address or phone number listed above, or by e-mail at michael.l.mccord@wrd.state.or.us.

Sincerely,

Michael L. McCord
Well Construction Specialist

c: Richard Edwards, NW Region Well Inspector

(7) Diagram showing the pertinent features of the proposed well design and construction (attach additional pages if needed):

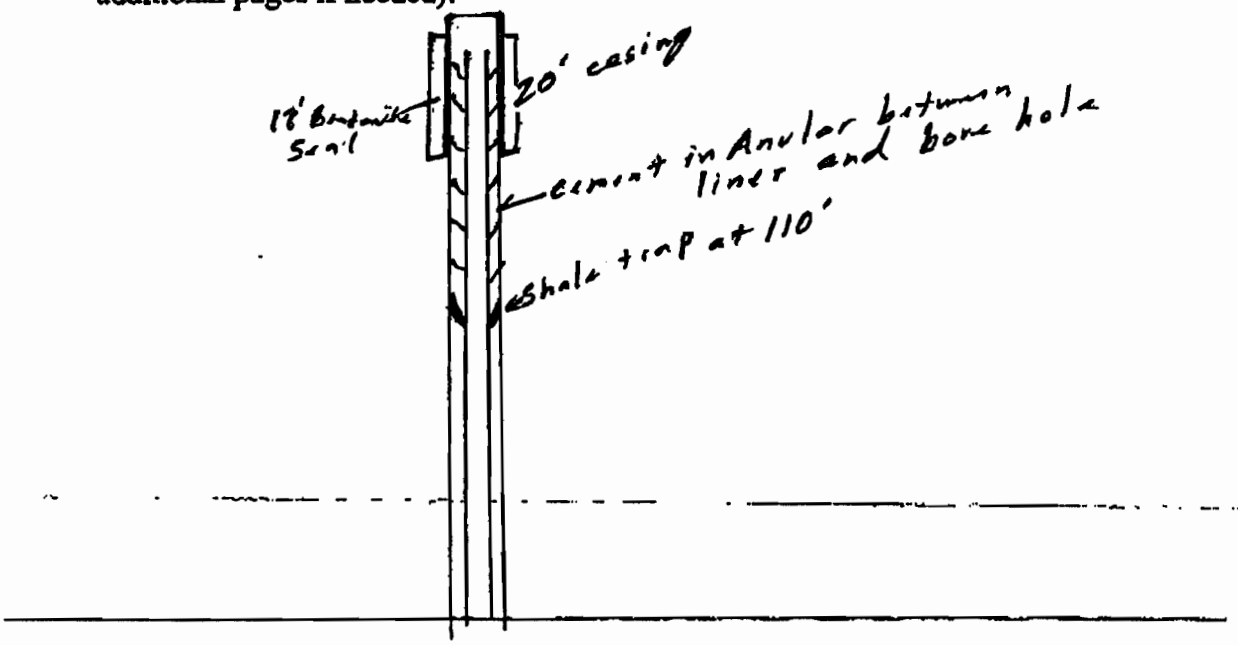

PLEASE NOTE:

(1) If approved, all other phases of well construction must comply with the appropriate standards described in OAR 690-200 through 690-240.

(2) If it should be determined at some future date that the well, due to its construction, is allowing groundwater contamination, waste or loss of artesian pressure, the undersigned shall return to the site and rectify the problem.

(3) If oral approval was granted, a written request must be submitted to the Department either within three (3) working days of the date of oral approval or prior to the completion of the associated well work. Failure to submit a written request as described above may void prior approval.

I have read and understand the above information. I further attest that the information provided is accurate to the best of my knowledge.

Bonded Constructor Signature: _____

For Water Resources Department Use Only

Date: 4-3-01

Approved by: _____ Denied by: _____

Remarks: _____

revised: 6-99
